

VERTICAL-LIFT TRACK

- BREAKAWAY
- STRAIGHT INCLINE (OPTIONAL)
- MAX. 100" DOOR HEIGHT


HEADROOM REQUIREMENTS:

MINIMUM HEADROOM =
 DOOR HEIGHT + 12" (BREAKAWAY TRACK)
 DOOR HEIGHT + 24" (STRAIGHT INCLINE TRACK)

12" ADDITIONAL HEADROOM REQUIRED FOR DOUBLE SHAFTS

NOTE:

SPRING SIZE AND CONFIGURATION INDIVIDUALLY CALCULATED TO COUNTERBALANCE DOOR LOAD. AN EXACT SPRING LAYOUT MAY REQUIRE 6" SPRINGS OR DOUBLE SHAFTS.

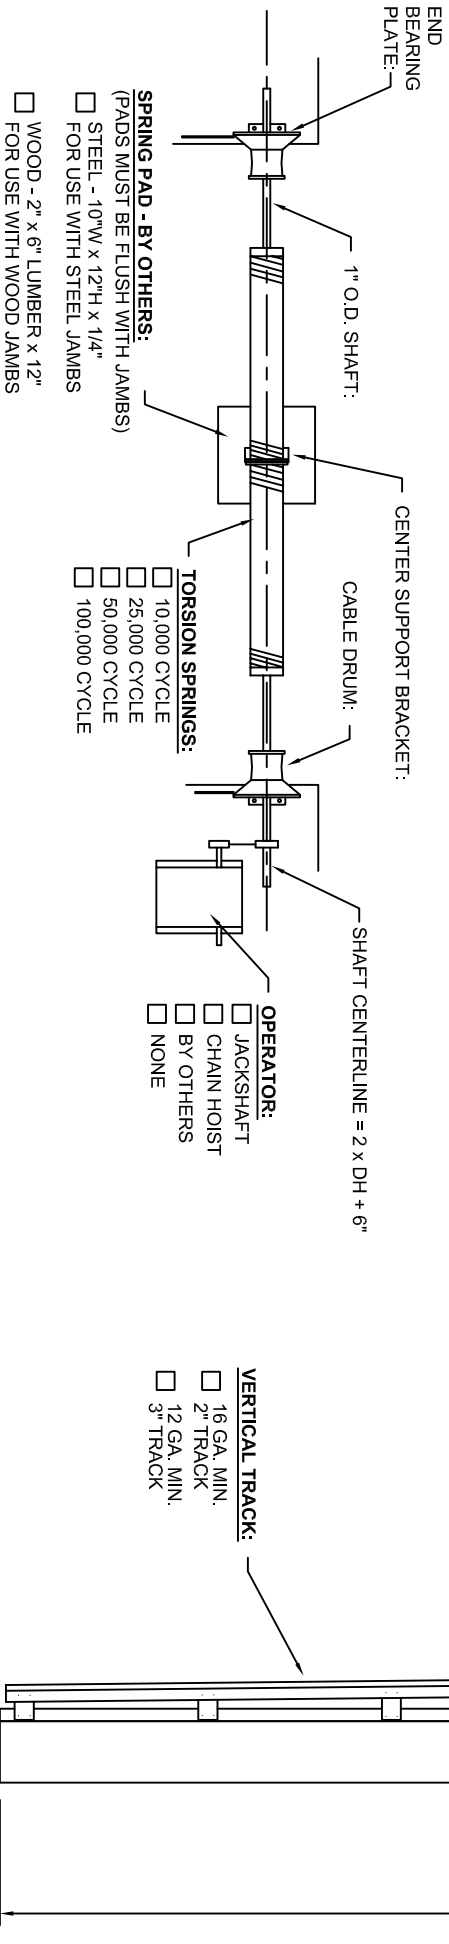

CUST:	VERTICAL LIFT	TRACK SIZE:	OPERATOR MODEL #:	OVERHEAD CLEARANCE:	SHEET 'T-7'
JOB:	OPENING SIZE: _____ " W x _____ " H		OPERATOR BACKROOM:	AVAILABLE HEADROOM:	DATE:
ARCH:	DOOR SIZE: _____ " W x _____ " H		BACK ROOM:	HEADROOM REQUIREMENT:	BID #:
CONT:					PAGE _____ of _____
